



Washoe County Regional Communication System


P25 Joint Operating Committee,
25 July 2024

LID SUMMARY BY AGENCY



<i>Agency</i>	<i>EDACS LIDS</i>	<i>P25 UID</i>	<i>Total # of Radios</i>
Reno Tahoe Airport Authority	238	281	281
US Drug enforcement Agency	24	24	24
Pyramid Lake Paiute Tribe	85	85	85
City of Reno	1083	1343	1343
Reno Sparks Indian Colony	71	72	72
City of Sparks	476	474	476
Truckee Meadows Fire & Rescue	348	331	348
Nevada System of Higher Education, UNR, TMCC	78	78	78
North Lake Fire Protection District	102	101	102
US Department of Veteran's Affairs	22	22	22
Truckee Meadows Water Authority	104	104	104*
Washoe County School District	809	1076	1076
Air National Guard	42	30	42
Washoe County	1453	1611	1611

Truckee Meadows Water Authority LID Reduction

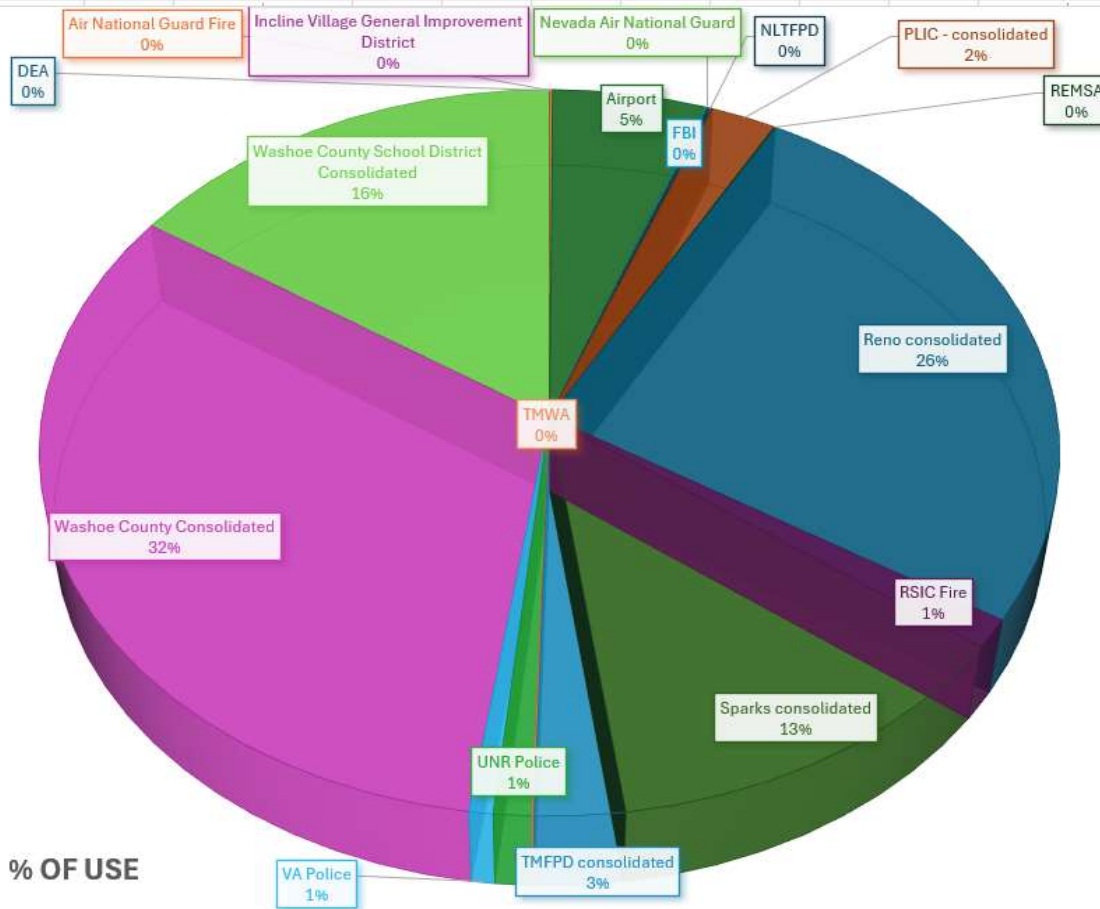

Radio Call Counts by Agency

Agencies

DEA	7,056
Air National Guard Fire	44,953
Airport	2,820,442
FBI	39,295
Incline Village General Improvement District	216
Nevada Air National Guard	11,939
NLTFPD	99,137
PLIC - consolidated	1,209,390
REMSA	28,051
Reno consolidated	13,737,238
RSIC Fire	674,366
Sparks consolidated	6,654,952
TMFPD consolidated	1,383,015
TMWA	35,128
UNR Police	578,281
VA Police	367,737
Washoe County Consolidated	17,051,557
Washoe County School District Consolidated	8,213,356


104 Assigned EDACS Lids

104 P25 LIDS

Reduced to 17 EDACS/P25 Radios

Nevada Shared Radio System Project Update: Region 1 Update

- Region 1 Cut-Over activities
 - Sites from Tonopah to Clark County are converting to P25
 - Activity started July 8th
 - There will be a 30 day burn-in period
 - No changes on the system while burn in occurs
 - Voice Quality is Crisp and Clear
 - The expectations was a Robotic sound: but the voice quality appears to be an improvement from EDACS.

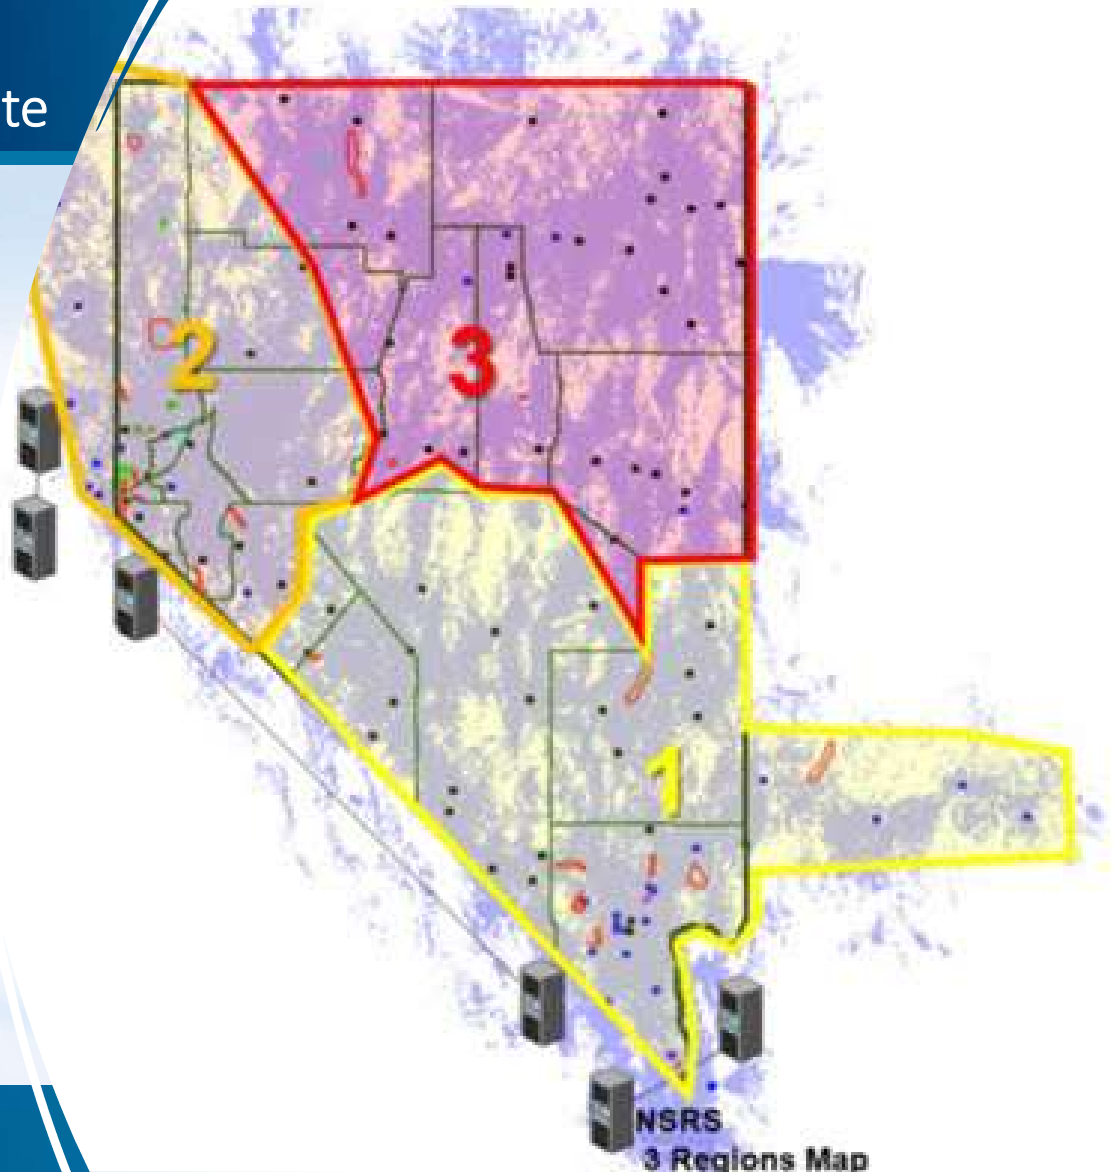


Nevada Shared Radio System Update for Region 2

- **Incline Sheriff's Office & Biltmore**
 - Permit approved by TRPA
 - RX3 Construction Completed
 - NVE Power addition to Incline Sheriff's and Communication H-frame Hook up for Site on Wheels
 - Biltmore Cabinet to be installed on Watertank APN
 - Foundation installed and Cabinet to be installed
 - Wave guide correction work to be completed during microwave installations
 - Microwave work to begin August 19th, 2024
- **Red Peak**
 - Lease agreement approved by BCC
 - Lease agreement effective in FY 25
 - Permitting expected to take 6 weeks.
 - **AWAITING NOTICE TO PROCEED FOR CONSTRUCTION FROM OWNER**



Nevada Shared Radio System Project Update: REGION 2

- **Marble Bluff**
 - Awaiting approval from Tribe to move forward with signing NVE Right of Way agreement.
 - 2 weeks remaining on construction work.
 - P25 Antenna installation to occur by September 2024
- **RX3**
 - Completed Biltmore
 - Load center connections to be made during the week of August 12th
- **Microwave Deployment (Outages will stay on Wednesdays)**
 - Snowflake ↔ Biltmore August 19 through August 23, 2024
 - Biltmore ↔ Slide August 26 through August 30th, 2024
- **DELAYED TO SPRING 2025****
 - Marble ↔ Poito
 - Poito ↔ Fox
 - Red Peak ↔ Spectrum
 - Red Peak ↔ Virginia

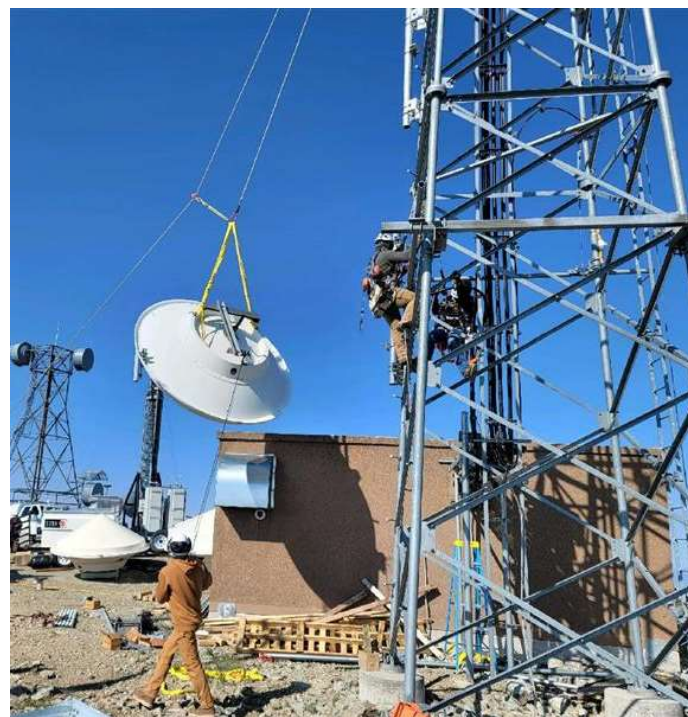

Nevada Shared Radio System Project Update: Project Pause



- Project Pause-
 - L3Harris is negotiating a program pause with the Nevada Shared Radio System (NSRS)
 - NSRS Members are unable to provide enough site to L3Harris for P25 Installation.
 - Details of Negotiation are **confidential** at this time.
 - Washoe County is not meeting scheduled timelines with site completions
 - BLM Permits : **Smokey Quartz & Seven Lakes**
 - **Ashfields** (stuck in JOC Committee for more than 18 months)
 - **Red Peak** (Owners has yet to send Notice to Proceed, and hasn't signed Lease agreement)
 - **Biltmore** (Completion of Cabinet installation and power expected by August for microwave deployment, no permanent solution created- awaiting schedule for EKN Astoria Waldorf Casino Build.)
 - **Marble Bluff** delays in Right Of Way agreement for NVE Power
 - **Mt Rose** delays in getting new ice bridge installed (site owner must approved design)
 - **Poito** awaiting site owner to move equipment to make room for Microwave and P25 equipment.



Questions & Concerns?

Melissa Lawney
Washoe County Regional
Communications Coordinator
230 Edison Way
Reno, NV 89502
(775) 858-5952

Thank you
